


**Project:** Anchor 3

**Test Date:** 09/04/2013

**Certificate No:** COV1323223

*This certificate is issued to GripplE Ltd to certify that the undersigned surveyor did, at their request attend the premises at The Old West Gun Works, Sheffield on and between the above dates for the purpose of examining and witnessing tests on the items listed below. All tests produced satisfactory results.*

## TEST CONFIGURATION

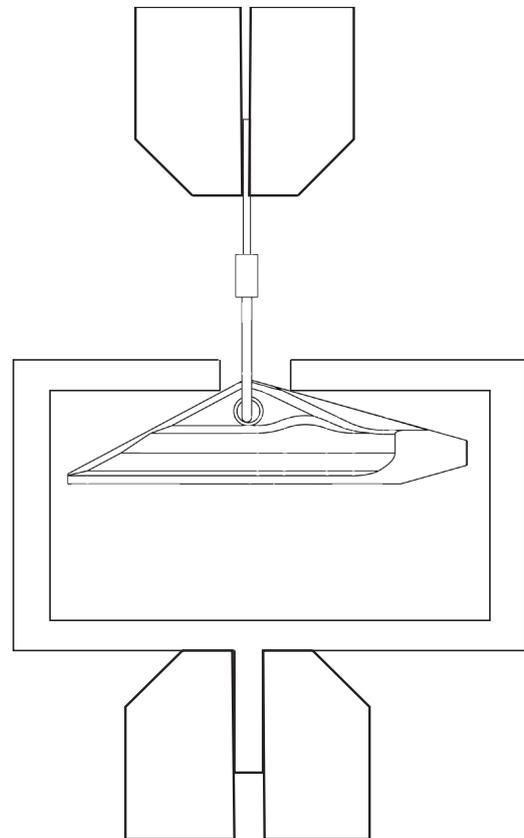

M Cobb  
Surveyor of Lloyd's Register

GripplE Model	Rope Construction	Load Rating*	Results*			Average*
Anchor 3	1x19 4mm ZnAl	500 kg 1,102 lbs	1,311 kg 2,890 lbs	1,187 kg 2,616 lbs	1,308 kg 2,883 lbs	1,268 kg 2,796 lbs

*\*Results indicate loads obtained in laboratory test conditions. Actual load ratings are always dependant on soil type and ground conditions at the installation site.*
